


PROJECT TIMELINE

Deer Run Park

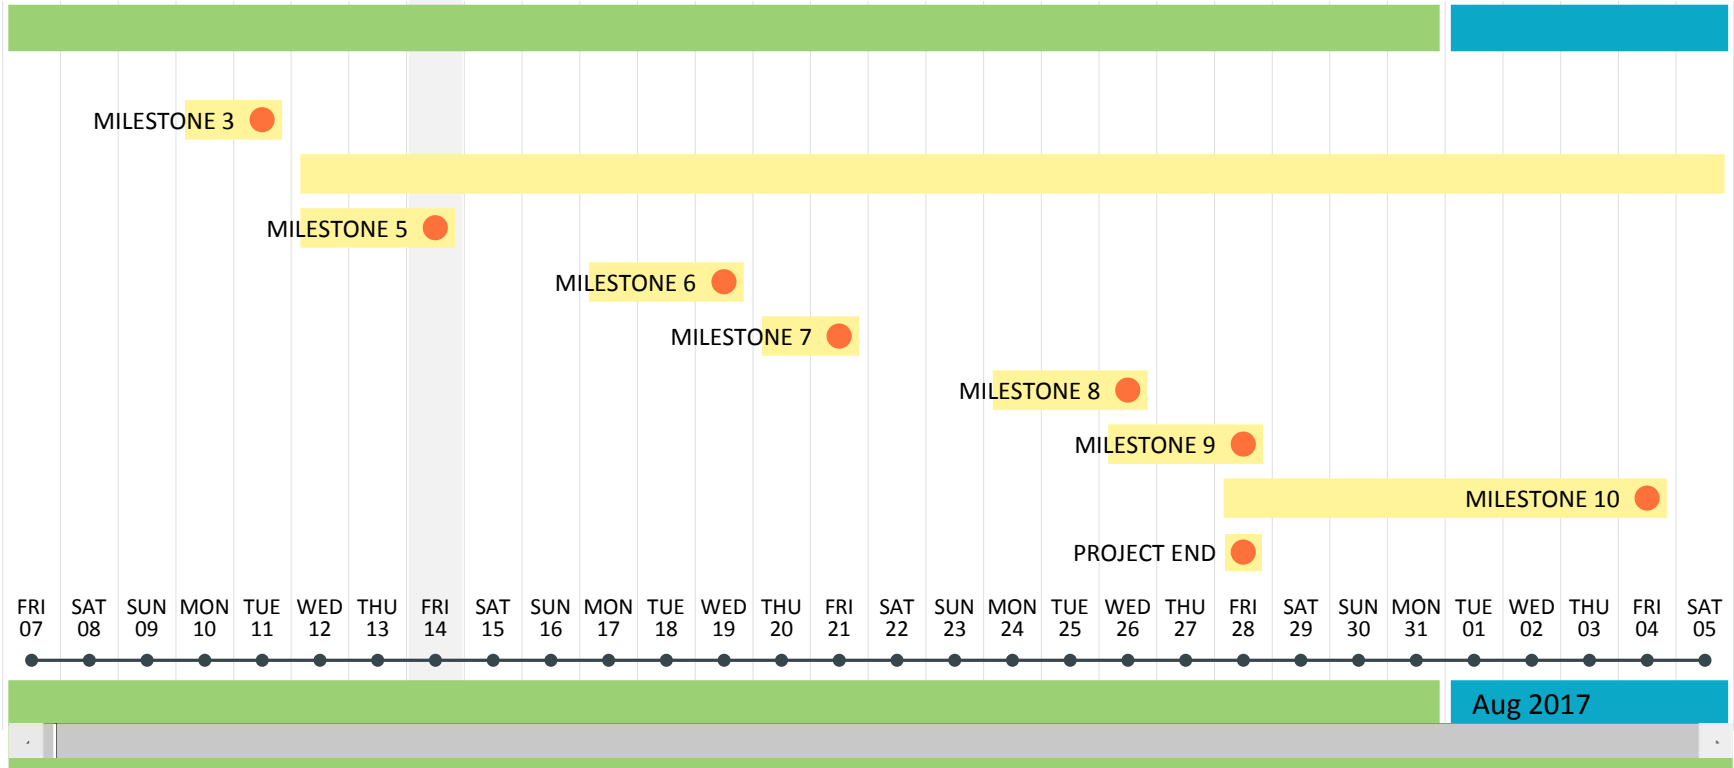

ENTER START DATE:

2017-07-04

ACTIVITY	START	END	NOTES
Project Start	2017-07-04		mobilize on site /tree protection/construction fence
Milestone 1	2017-07-05	2017-07-05	Excavation and sub grade inspection
Milestone 2	2017-07-06	2017-07-06	Civil works /splash pad granulars/insulation and forms install

ACTIVITY	START	END	NOTES
Milestone 3	2017-07-10	2017-07-11	mechanical plumbing on splash pad
Milestone 4	2017-07-12	28//07/2017	Electrical works
Milestone 5	2017-07-12	2017-07-14	form and pour footings /concrete pad and bike rack
Milestone 6	2017-07-17	2017-07-19	Grounding of splash pad /pour splash pad
Milestone 7	2017-07-20	2017-07-21	pavers install
Milestone 8	2017-07-24	2017-07-26	fine grade burms /asphalt
Milestone 9	2017-07-26	2017-07-28	soft landscaping /planting /site furniture install
Milestone 10	2017-07-28	2017-08-04	closer out documents /final inspections/warranty
Project End	2017-07-28		
